

June 2009 Progress Report on the Abatement and Deconstruction of 130 Liberty Street

Below is the June 2009 monthly progress report on the abatement and deconstruction of 130 Liberty Street. This report includes updates on the progress of work in the building and future milestones in the abatement and deconstruction process.

130 Liberty Street Progress and Milestones as of June 10, 2009

Abatement Status


- Abatement is complete on all floors through and including the 4th floor.
- As indicated in last month's report, floors 2 and 3 should be abated by next week. The first floor and certain areas of the basement should be complete by end of this month.
- The building facade has been removed down through and including the 6thth floor, and is scheduled to be removed through the 3rd floor by July 1, 2009.
- Bovis, the contractor for this job has indicated that the facade will be removed entirely by mid July 2009.

Deconstruction Status

- The Implementation Plan for deconstruction and the Environment, Health and Safety Plan and Emergency Action Plan has been approved by the regulatory team. The plans, public comments, and responses to public comments have been posted on the LMDC website (www.renewnyc.com).
- Bovis estimates that deconstruction will resume in mid-July 2009.
- Bovis has indicated that deconstruction will take 6 months to complete.

130 Liberty Street Deconstruction and Abatement Status

130 LIBERTY STREET

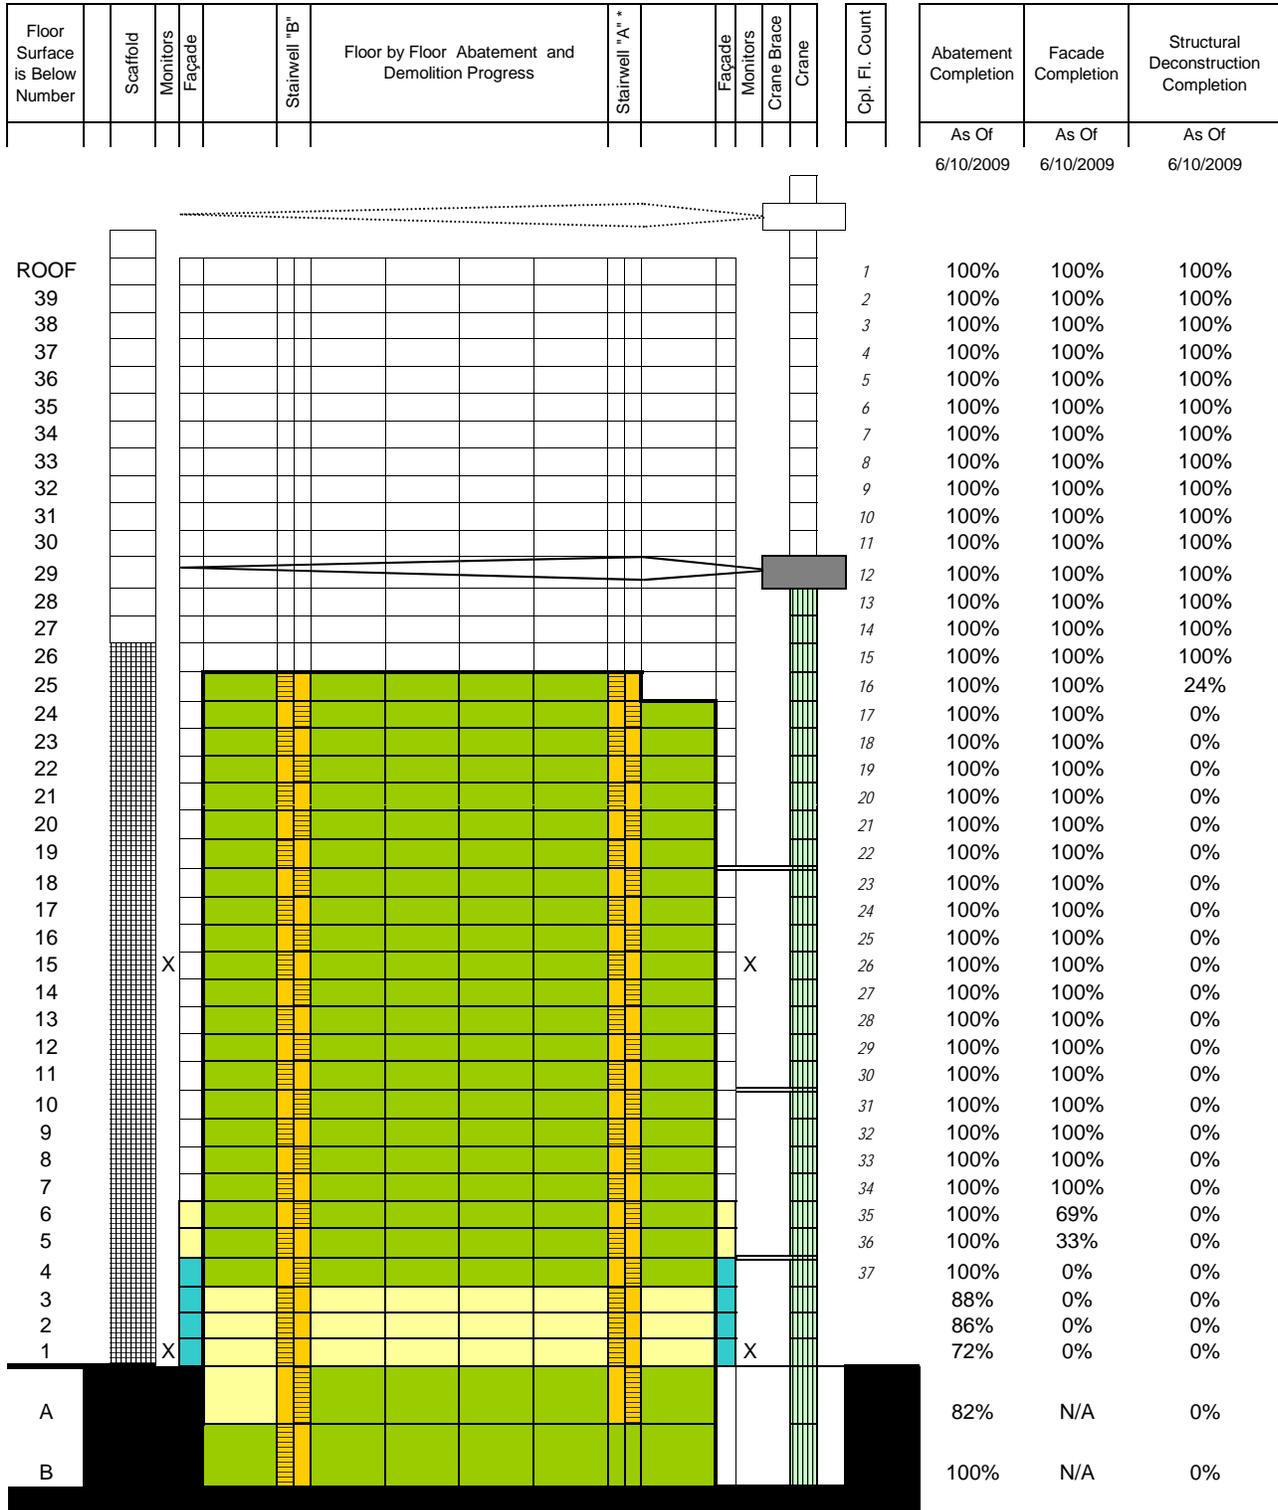

- KEY:
- Deconstructed
 - Abated, Inspected and Cleared
 - Abatement In Progress
 - Abatement Prep In Progress
 - Stairways
 - Façade Work
 - X Level III Air Monitor Locations
